ID	Task Name	Duration	Start	Finish	Predecess	Resource Names
1	**Mezeo for BlackBerry Project Plan**	**60 days**	**Mon 6/9/08**	**Mon 9/1/08**		
2	**Dependency 0**	**0 days**	**Fri 6/27/08**	**Fri 6/27/08**		
3	Icons and images	0 days	Fri 6/27/08	Fri 6/27/08		
4	**Design/Documentation Phase**	**15 days**	**Mon 6/9/08**	**Fri 6/27/08**		
5	Review of SRS	3 days	Mon 6/9/08	Wed 6/11/08		D1,D2,D3
6	Technical Design and Review	3 days	Thu 6/12/08	Mon 6/16/08	5	D1,D2,D3
7	Create Design document	4 days	Tue 6/17/08	Fri 6/20/08	6	D1,D2,D3
8	Mezeo server access from BB simulator	5 days	Mon 6/23/08	Fri 6/27/08		D2,D3
9	Create Test Plan	10 days	Mon 6/16/08	Fri 6/27/08		T1
10	GUI Prototype	5 days	Mon 6/23/08	Fri 6/27/08	7	D1
11	**Milestone 0**	**0 days**	**Mon 6/30/08**	**Mon 6/30/08**		
12	**Milestone 0 Deliverables**	**0 days**	**Mon 6/30/08**	**Mon 6/30/08**	10	
13	GUI Prototype Round 1	0 days	Mon 6/30/08	Mon 6/30/08		
14	Finalized Design document	0 days	Mon 6/30/08	Mon 6/30/08	4	
15	Final Acceptance Test Plan	0 days	Mon 6/30/08	Mon 6/30/08		
16						
17	**Dependency 1**	**0 days**	**Wed 7/2/08**	**Wed 7/2/08**		
18	Feedback on GUI Prototype	0 days	Wed 7/2/08	Wed 7/2/08		Client
19	Feedback on design document	0 days	Wed 7/2/08	Wed 7/2/08		Client
20	Final date for receiving logos and images	0 days	Wed 7/2/08	Wed 7/2/08		Client
21	Feedback on Acceptance Test Plan	0 days	Wed 7/2/08	Wed 7/2/08		Client
22	**Mezeo Main**	**12 days**	**Mon 6/30/08**	**Tue 7/15/08**	4	
23	Code for Mezeo Main	4 days	Mon 6/30/08	Thu 7/3/08	4	D1
24	Implement ExceptionHandler	3 days	Fri 7/4/08	Tue 7/8/08	23	D1
25	Handling Localization	2 days	Wed 7/9/08	Thu 7/10/08	24	D1
26	Multi-threading	2 days	Fri 7/11/08	Mon 7/14/08	25	D1
27	Unit Testing	1 day	Tue 7/15/08	Tue 7/15/08	26	D1
28	**Mezeo Core**	**5 days**	**Mon 6/30/08**	**Fri 7/4/08**	4	
29	Application Flow Logic Phase 1	2 days	Mon 6/30/08	Tue 7/1/08	4	D2
30	Model Object for Users	1 day	Wed 7/2/08	Wed 7/2/08	29	D2
31	Model Object for Errors	1 day	Thu 7/3/08	Thu 7/3/08	30	D2
32	Unit Testing	1 day	Fri 7/4/08	Fri 7/4/08	31	D2
33	**Communication Engine**	**8 days**	**Mon 6/30/08**	**Wed 7/9/08**	4	
34	Mezeo API Wrapper structure	4 days	Mon 6/30/08	Thu 7/3/08	4	D3
35	Operations for User Resource Type (login, info)	2 days	Fri 7/4/08	Mon 7/7/08	34	D3
36	HTTP Implementation	2 days	Mon 7/7/08	Tue 7/8/08	32	D2
37	Unit Testing	1 day	Wed 7/9/08	Wed 7/9/08	36	D2
38	**GUI Engine**	**4 days**	**Tue 7/8/08**	**Fri 7/11/08**		
39	Login Screen	1 day	Tue 7/8/08	Tue 7/8/08	35	D3

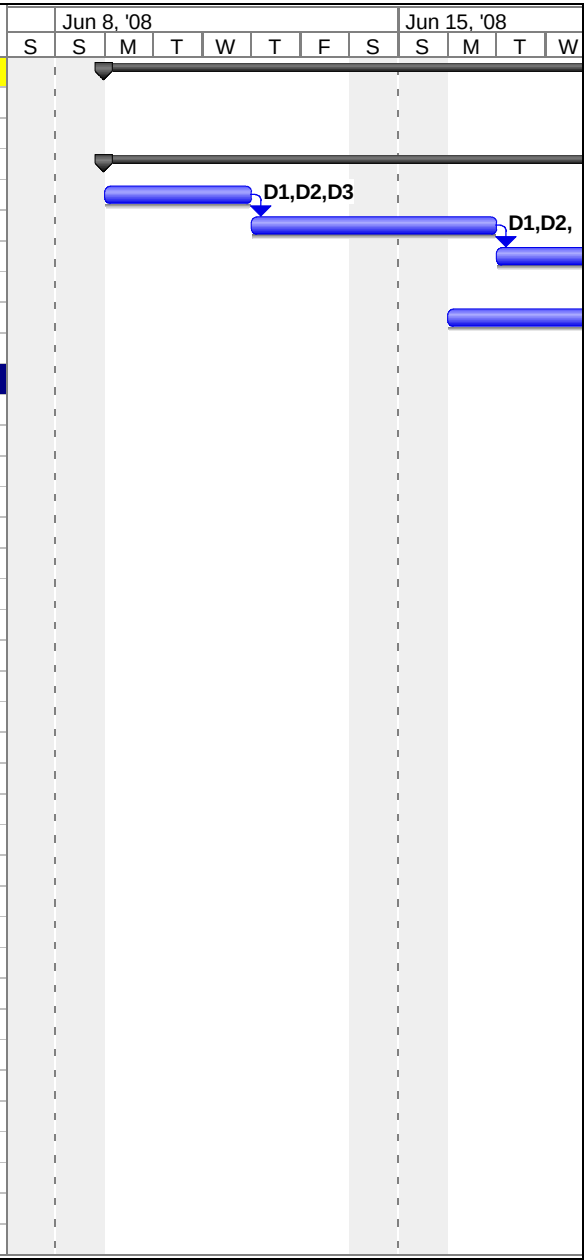

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
40	My Account Screen	2 days	Thu 7/10/08	Fri 7/11/08	30,33	D2
41	Notifications and Alerts	0.5 days	Wed 7/9/08	Wed 7/9/08	39	D3
42	Context sensitive menus	1.5 days	Wed 7/9/08	Thu 7/10/08	41	D3
43	Unit Testing	1 day	Fri 7/11/08	Fri 7/11/08	42	D3
44	Code Review	2 days	Wed 7/16/08	Thu 7/17/08	22,4	D4
45	**Testing**	**10 days**	**Mon 6/30/08**	**Fri 7/11/08**		
47	Milestone 1	0 days	Tue 7/15/08	Tue 7/15/08		
48						
49	**Dependency 2**	**0 days**	**Fri 7/18/08**	**Fri 7/18/08**		
50	Feedback on Milestone 1	0 days	Fri 7/18/08	Fri 7/18/08		Client
51	Wireframes for Orientation Wizards	0 days	Fri 7/18/08	Fri 7/18/08		
52	**Mezeo Core**	**7 days**	**Wed 7/16/08**	**Thu 7/24/08**		
53	Application Flow Logic Phase 2	3 days	Wed 7/16/08	Fri 7/18/08	27	D1
54	Model Object for Files	2 days	Mon 7/21/08	Tue 7/22/08	53	D1
55	Model Object for Projects	0.5 days	Wed 7/23/08	Wed 7/23/08	54	D1
56	Model Object for Applications	0.5 days	Wed 7/23/08	Wed 7/23/08	55	D1
57	Unit Testing	1 day	Thu 7/24/08	Thu 7/24/08	56	D1
58	**Communication Engine**	**5 days**	**Mon 7/14/08**	**Fri 7/18/08**	**33**	
59	Operations for File/Folder Resource Type	2 days	Mon 7/14/08	Tue 7/15/08	40	D2
60	Operations for Project Resource Type	1 day	Wed 7/16/08	Wed 7/16/08	59	D2
61	Operations for Public Resource Type	1 day	Thu 7/17/08	Thu 7/17/08	60	D2
62	Unit Testing	1 day	Fri 7/18/08	Fri 7/18/08	61	D2
63	**GUI Engine**	**12 days**	**Mon 7/14/08**	**Tue 7/29/08**	**38**	
64	Carousel widget (navigation, graphics, invoking sc	4 days	Mon 7/14/08	Thu 7/17/08	43	D3
65	File/folder operations (listing, upload, download, de	5 days	Mon 7/21/08	Fri 7/25/08	62	D2
66	Home Screen - MRS/MRF functionality	3 days	Fri 7/25/08	Tue 7/29/08	57	D1
67	Handling Progress bar	2 days	Fri 7/18/08	Mon 7/21/08	64	D3
68	Unit Testing	1 day	Mon 7/28/08	Mon 7/28/08	65	D2
69	**Device Manager**	**2 days**	**Tue 7/22/08**	**Wed 7/23/08**		
70	Local File Manager	2 days	Tue 7/22/08	Wed 7/23/08	67	D3
71	**Incorporating Client Feedback**	**3 days**	**Thu 7/24/08**	**Mon 7/28/08**		
72	For GUI Engine	3 days	Thu 7/24/08	Mon 7/28/08	70	D3
73	Code Review	3 days	Fri 7/18/08	Tue 7/22/08	33	D4
74	**Testing**	**10 days**	**Thu 7/17/08**	**Wed 7/30/08**		
75	Testing on OS 4.2, 4.3	10 days	Thu 7/17/08	Wed 7/30/08	45	T1
76	Milestone 2	1 day	Wed 7/30/08	Wed 7/30/08	52,58,63,7	
77						
78	**Dependency 3**	**0 days**	**Mon 8/4/08**	**Mon 8/4/08**		
79	Feedback on Milestone 2	0 days	Mon 8/4/08	Mon 8/4/08	76	Client



Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
80	**Mezeo Core**	**3 days**	**Wed 7/30/08**	**Fri 8/1/08**	**52**	
81	Model Object for Potluck	1 day	Wed 7/30/08	Wed 7/30/08	66	D1
82	Model Object for Groups	1 day	Thu 7/31/08	Thu 7/31/08	81	D1
83	Unit Testing	1 day	Fri 8/1/08	Fri 8/1/08	82	D1
84	**Communication Engine**	**3 days**	**Tue 7/29/08**	**Thu 7/31/08**	**58**	
85	Operations for Potluck Resource Type	1 day	Tue 7/29/08	Tue 7/29/08	72	D3
86	Operations for Groups Resource Type	1 day	Wed 7/30/08	Wed 7/30/08	85	D3
87	Unit Testing	1 day	Thu 7/31/08	Thu 7/31/08	86	D3
88	**GUI Engine**	**8 days**	**Tue 7/29/08**	**Thu 8/7/08**		
89	File Sharing	7 days	Tue 7/29/08	Wed 8/6/08	68	D2
90	New Members	3 days	Fri 8/1/08	Tue 8/5/08	87	D3
91	Project listing	1.5 days	Mon 8/4/08	Tue 8/5/08	83	D1
92	Context Menus	1.5 days	Tue 8/5/08	Wed 8/6/08	91	D1
93	Unit Testing	1 day	Thu 8/7/08	Thu 8/7/08	89	D2
94	**Device Manager**	**4 days**	**Wed 8/6/08**	**Mon 8/11/08**		
95	Native Application Manager	3 days	Wed 8/6/08	Fri 8/8/08	90	D3
96	Unit Testing	1 day	Mon 8/11/08	Mon 8/11/08	95	D3
97	Code Review	3 days	Tue 8/5/08	Thu 8/7/08		D4
98	**Incorporating Client Feedback and Code Review U**	**4 days**	**Thu 8/7/08**	**Tue 8/12/08**		
99	Communication Engine Updates	1 day	Fri 8/8/08	Fri 8/8/08	93	D2
100	Mezeo Core and Device Manager Updates	1 day	Tue 8/12/08	Tue 8/12/08	96	D3
101	GUI Engine Updates	2 days	Thu 8/7/08	Fri 8/8/08	92	D1
102	**Testing**	**10 days**	**Thu 7/31/08**	**Wed 8/13/08**	**74**	
103	Testing on OS 4.2, 4.3, 4.5	10 days	Thu 7/31/08	Wed 8/13/08	74	T1
104	Milestone 3	0 days	Thu 8/14/08	Thu 8/14/08		
105						
106	**Dependency 4**	**0 days**	**Wed 8/20/08**	**Wed 8/20/08**		
107	Feedback on Milestone 3	0 days	Wed 8/20/08	Wed 8/20/08		Client
108	**GUI Engine**	**11 days**	**Mon 8/11/08**	**Tue 8/26/08**		
109	File Sending Via (Bluetooth, Beam, Email, Text)	6 days	Mon 8/11/08	Tue 8/19/08	101	D1
110	Orientation screens and flow	5 days	Mon 8/11/08	Mon 8/18/08	99	D2
111	Context menus for screens	2 days	Wed 8/13/08	Thu 8/14/08	100	D3
112	Error handling	3 days	Wed 8/20/08	Fri 8/22/08	109	D1
113	Information Messages	2 days	Tue 8/19/08	Wed 8/20/08	110	D2
114	Unit Testing	2 days	Mon 8/25/08	Tue 8/26/08	112	D1
115	**Device Manager**	**4 days**	**Mon 8/18/08**	**Thu 8/21/08**		
116	Persisting applciation data	3 days	Mon 8/18/08	Wed 8/20/08	111	D3
117	Unit Testing	1 day	Thu 8/21/08	Thu 8/21/08	116	D3
118	Code Review	2 days	Fri 8/22/08	Mon 8/25/08		D4



Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

ID	Task Name	Duration	Start	Finish	Predecess	Resource Names
119	**Incorporating Client Feedback and Code Review U**	**3 days**	**Thu 8/21/08**	**Mon 8/25/08**		
120	Communication Engine Updates	0.5 days	Thu 8/21/08	Thu 8/21/08	113	D2
121	Mezeo Core Updates	0.5 days	Thu 8/21/08	Thu 8/21/08	120	D2
122	Device Manager Updates	1 day	Fri 8/22/08	Fri 8/22/08	117	D3
123	GUI Engine Updates	1 day	Mon 8/25/08	Mon 8/25/08	122	D3
124	**Testing**	**8 days**	**Thu 8/14/08**	**Tue 8/26/08**		
125	Testing on OS 4.2, 4.3, 4.5	8 days	Thu 8/14/08	Tue 8/26/08	102	T1
126	Milestone 4	0 days	Tue 8/26/08	Tue 8/26/08		
127						
128	**Dependency 5**	**0 days**	**Thu 8/28/08**	**Thu 8/28/08**		
129	Feedback on Milestone 4	0 days	Thu 8/28/08	Thu 8/28/08		Client
130	**Final Release**	**7 days**	**Fri 8/22/08**	**Mon 9/1/08**		
131	Bug fixes	5 days	Fri 8/22/08	Thu 8/28/08	121	D2
132	Code review and Client Feedback	5 days	Tue 8/26/08	Mon 9/1/08	123	D3
133	Optimizations	4 days	Wed 8/27/08	Mon 9/1/08	114	D1
134	**Testing**	**4 days**	**Wed 8/27/08**	**Mon 9/1/08**	**124**	
135	Testing on OS 4.2, 4.3, 4.5	4 days	Wed 8/27/08	Mon 9/1/08	124	T1
136	Milestone 5	0 days	Mon 9/1/08	Mon 9/1/08	130,134	

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

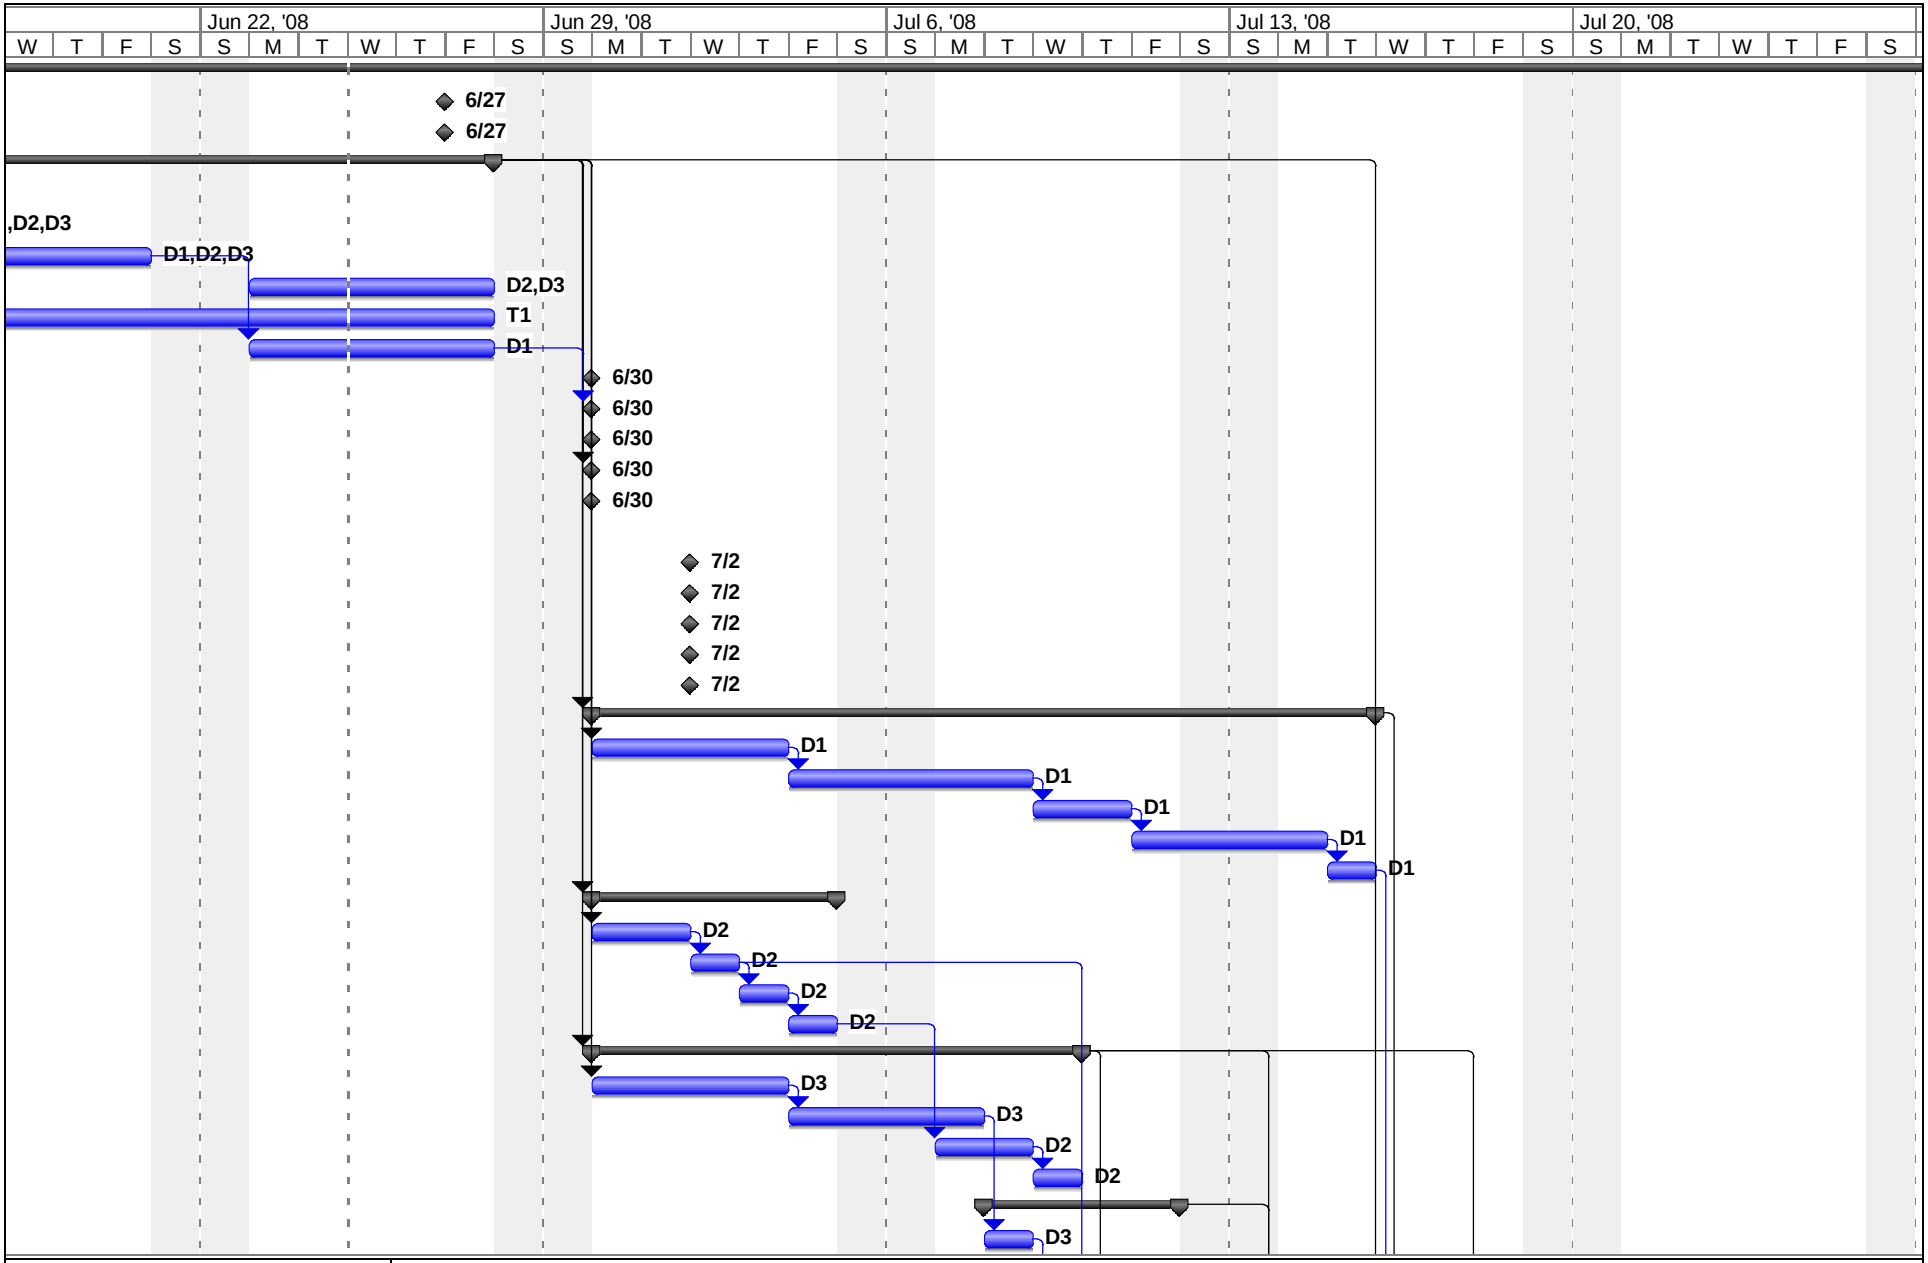

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

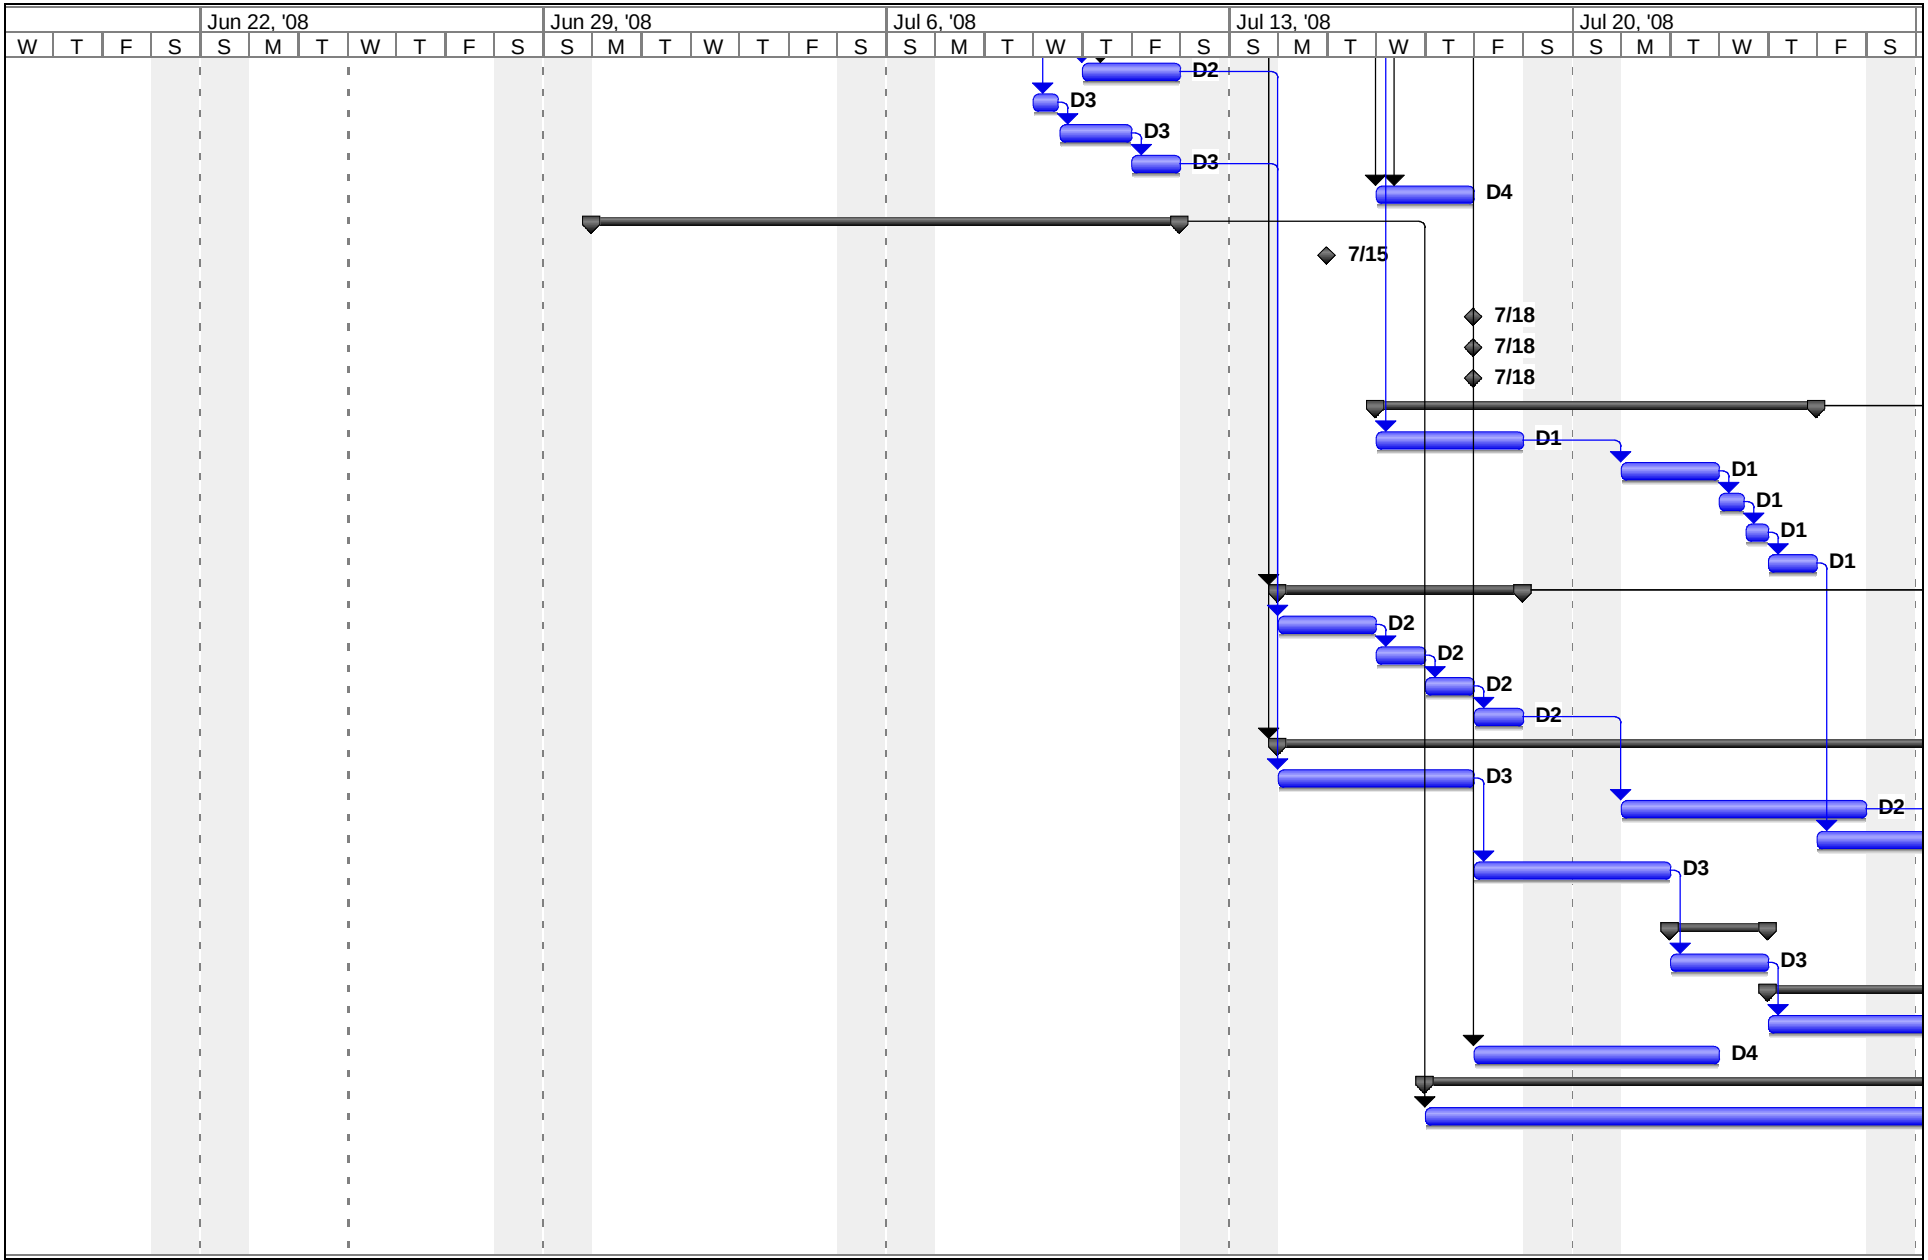

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

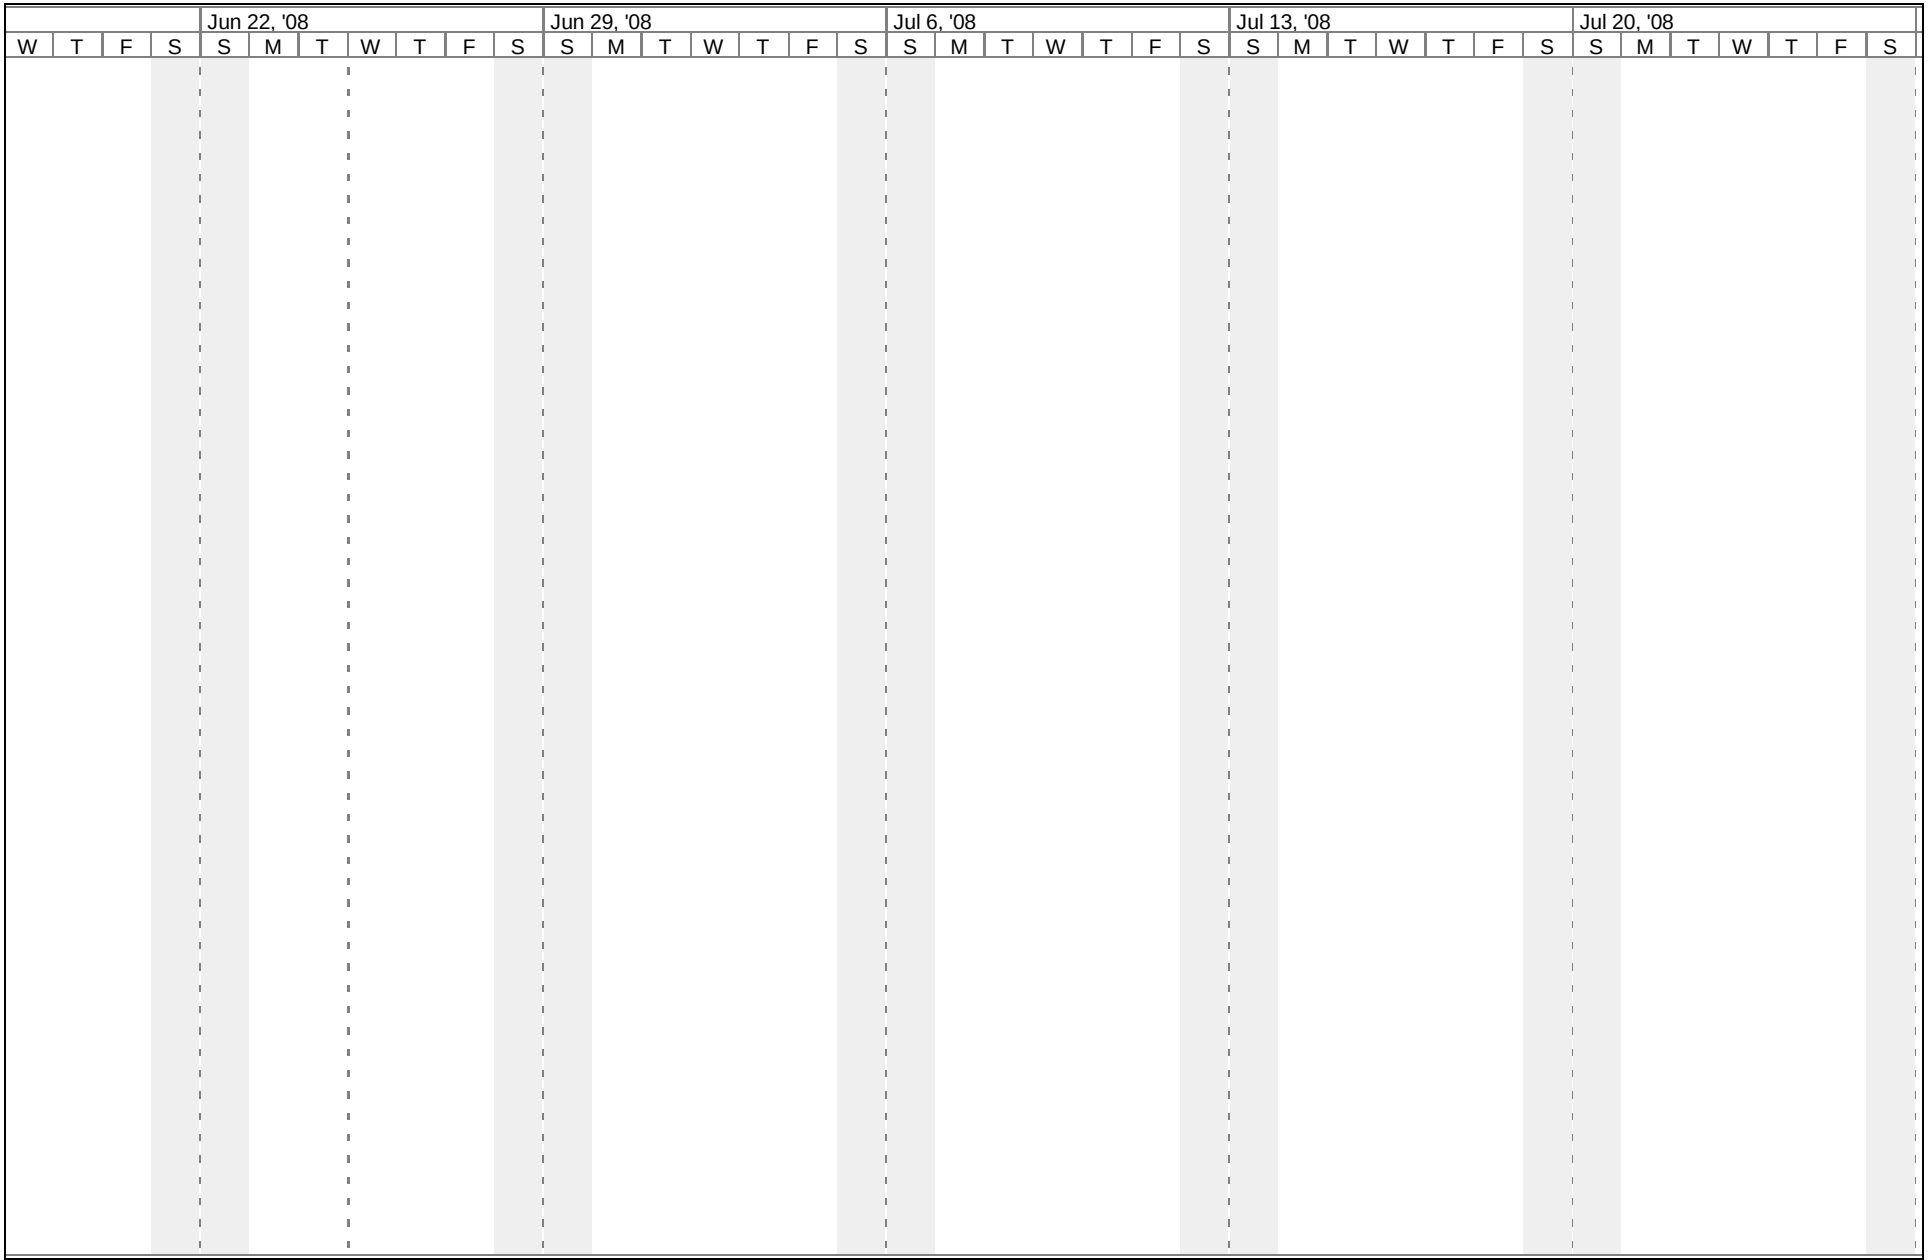
Jun 22, '08
Jun 29, '08
Jul 6, '08
Jul 13, '08
Jul 20, '08
W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08
Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

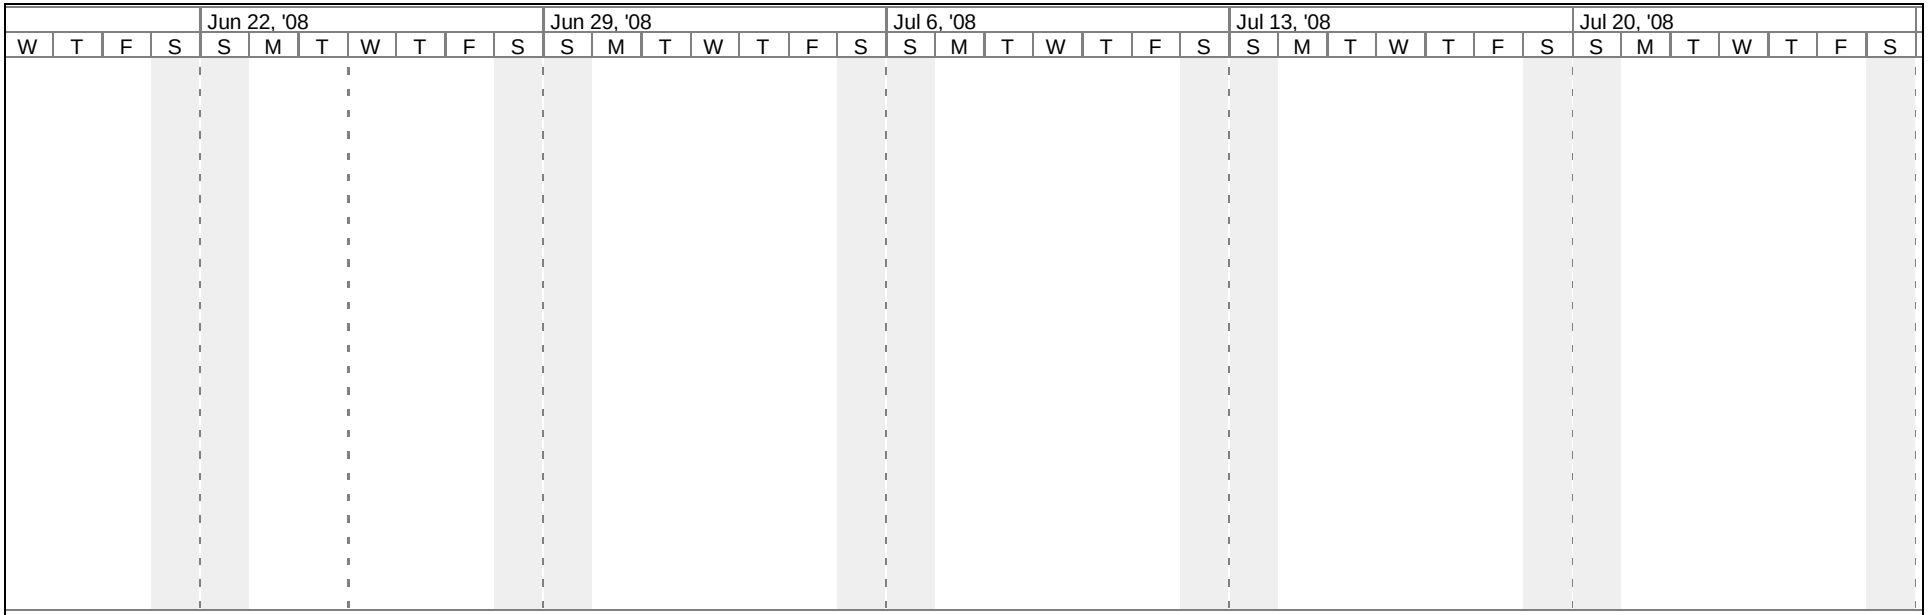

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

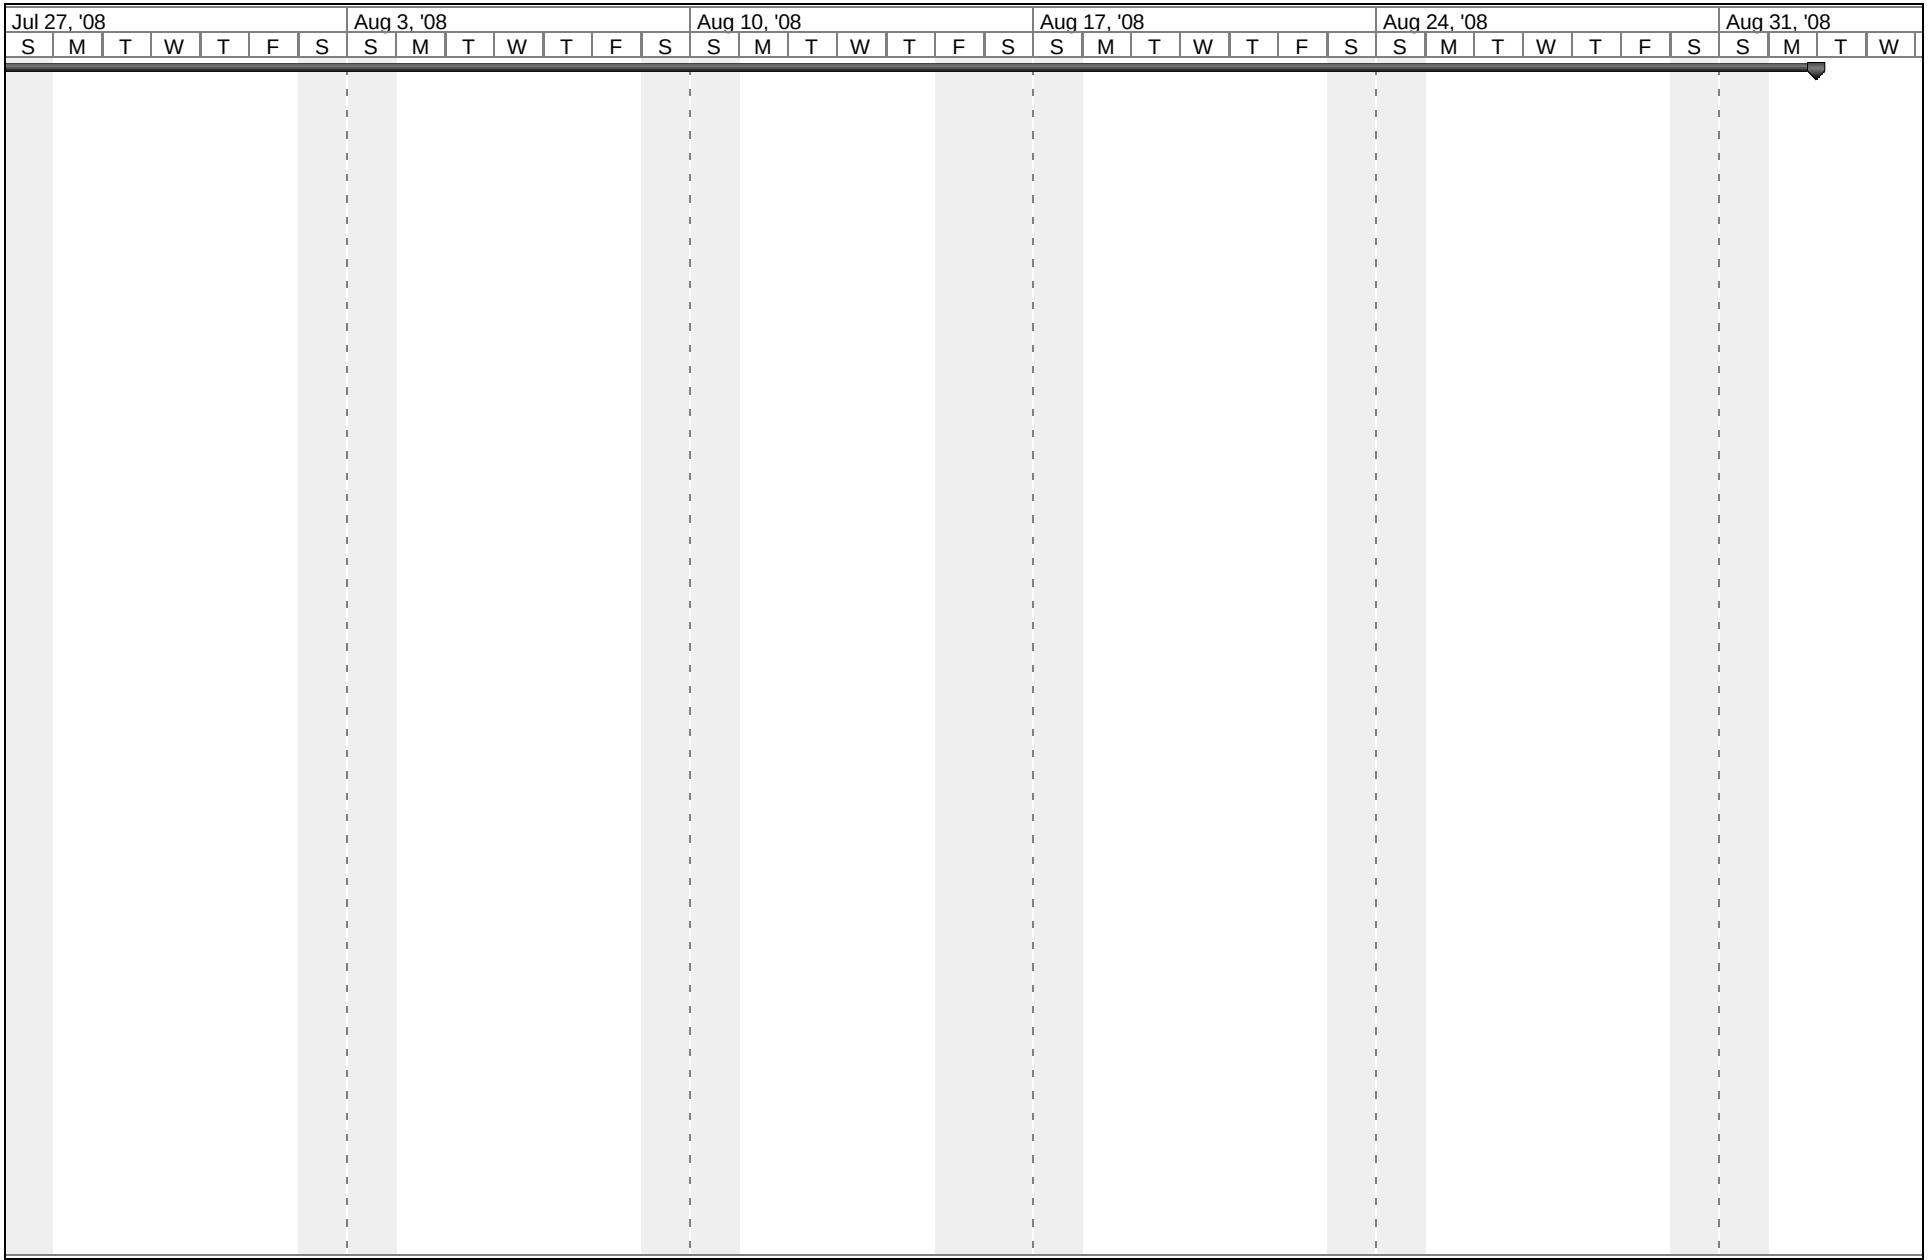

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

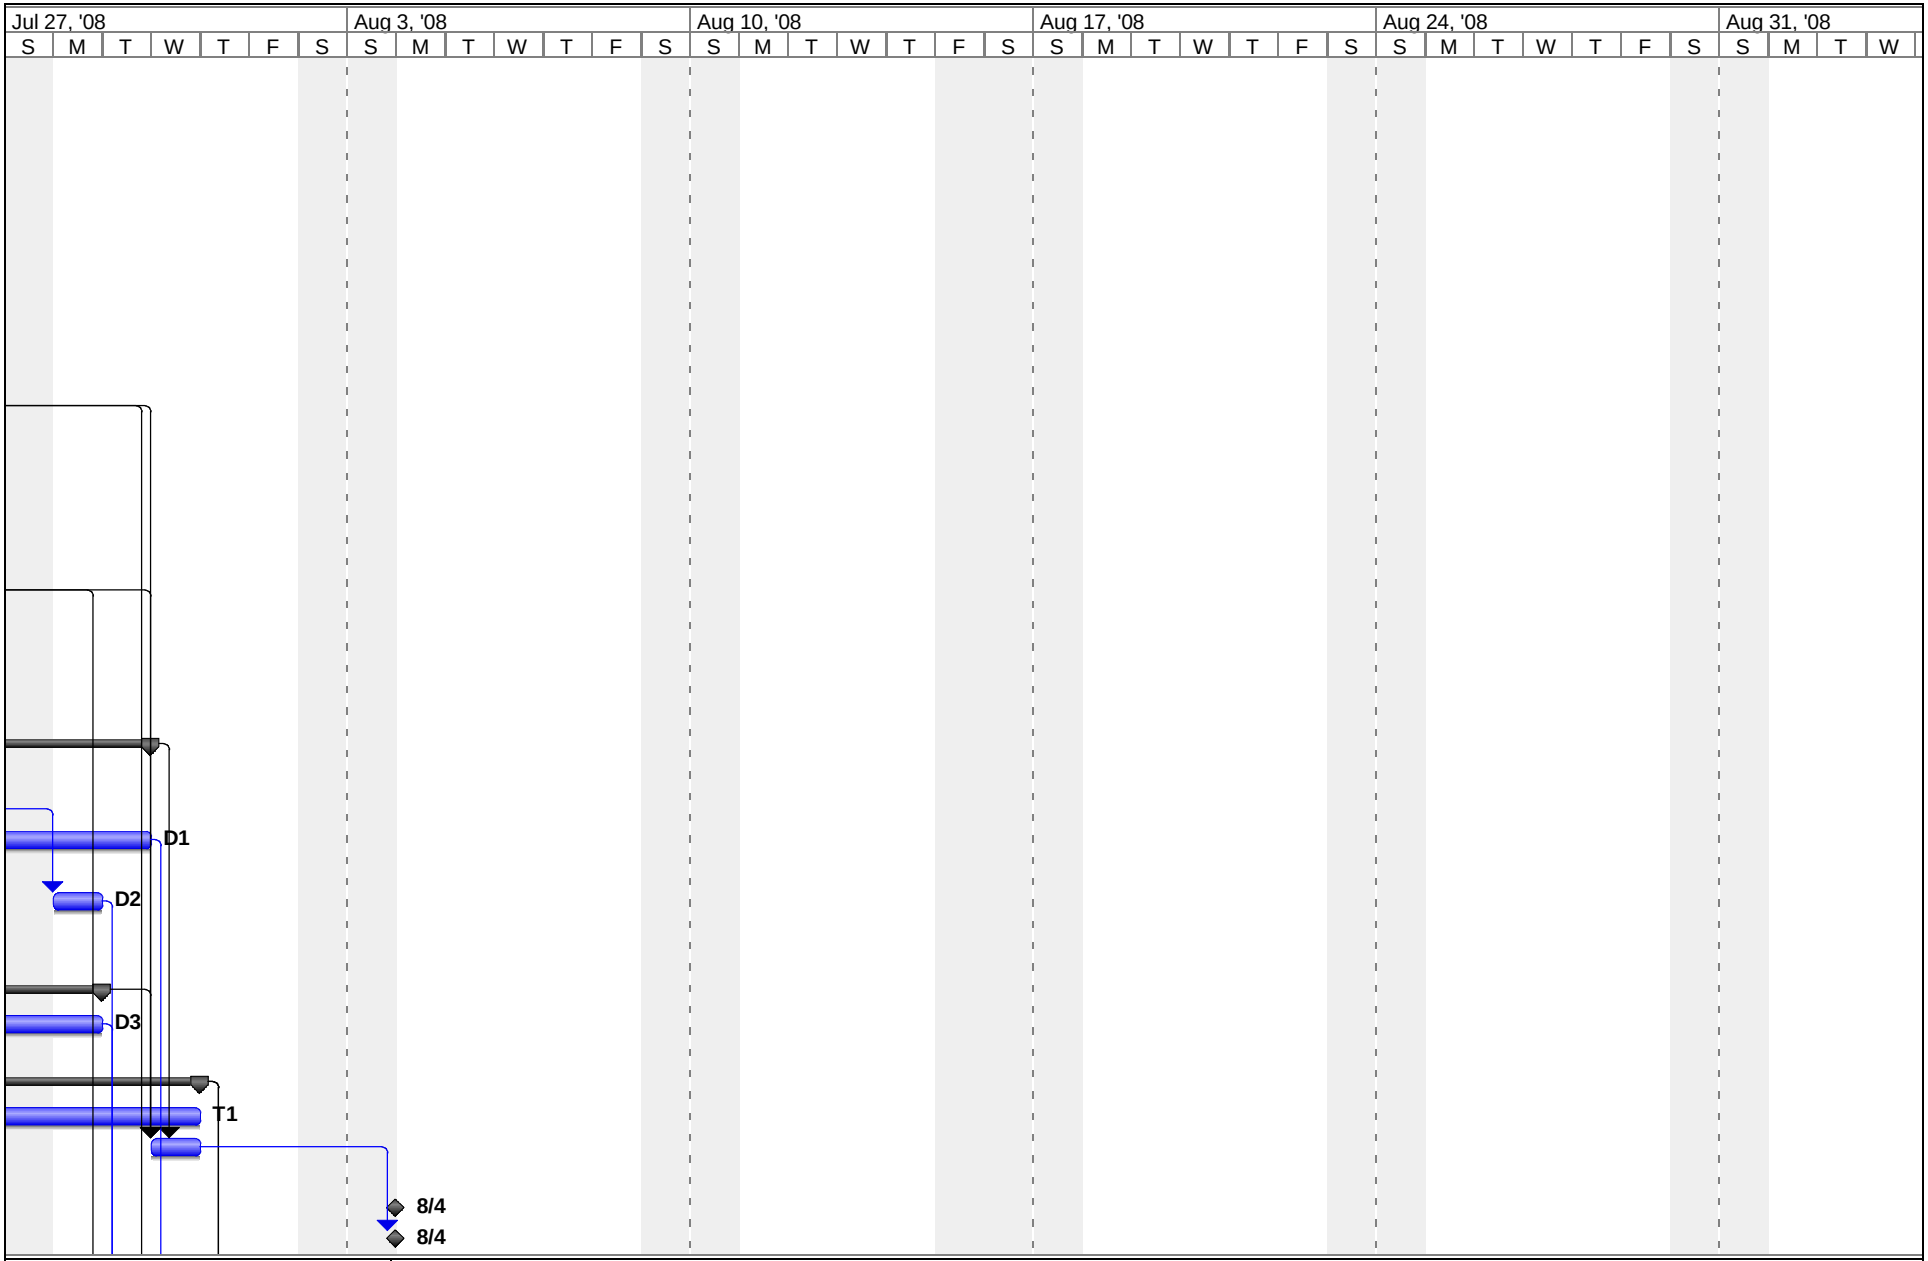

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

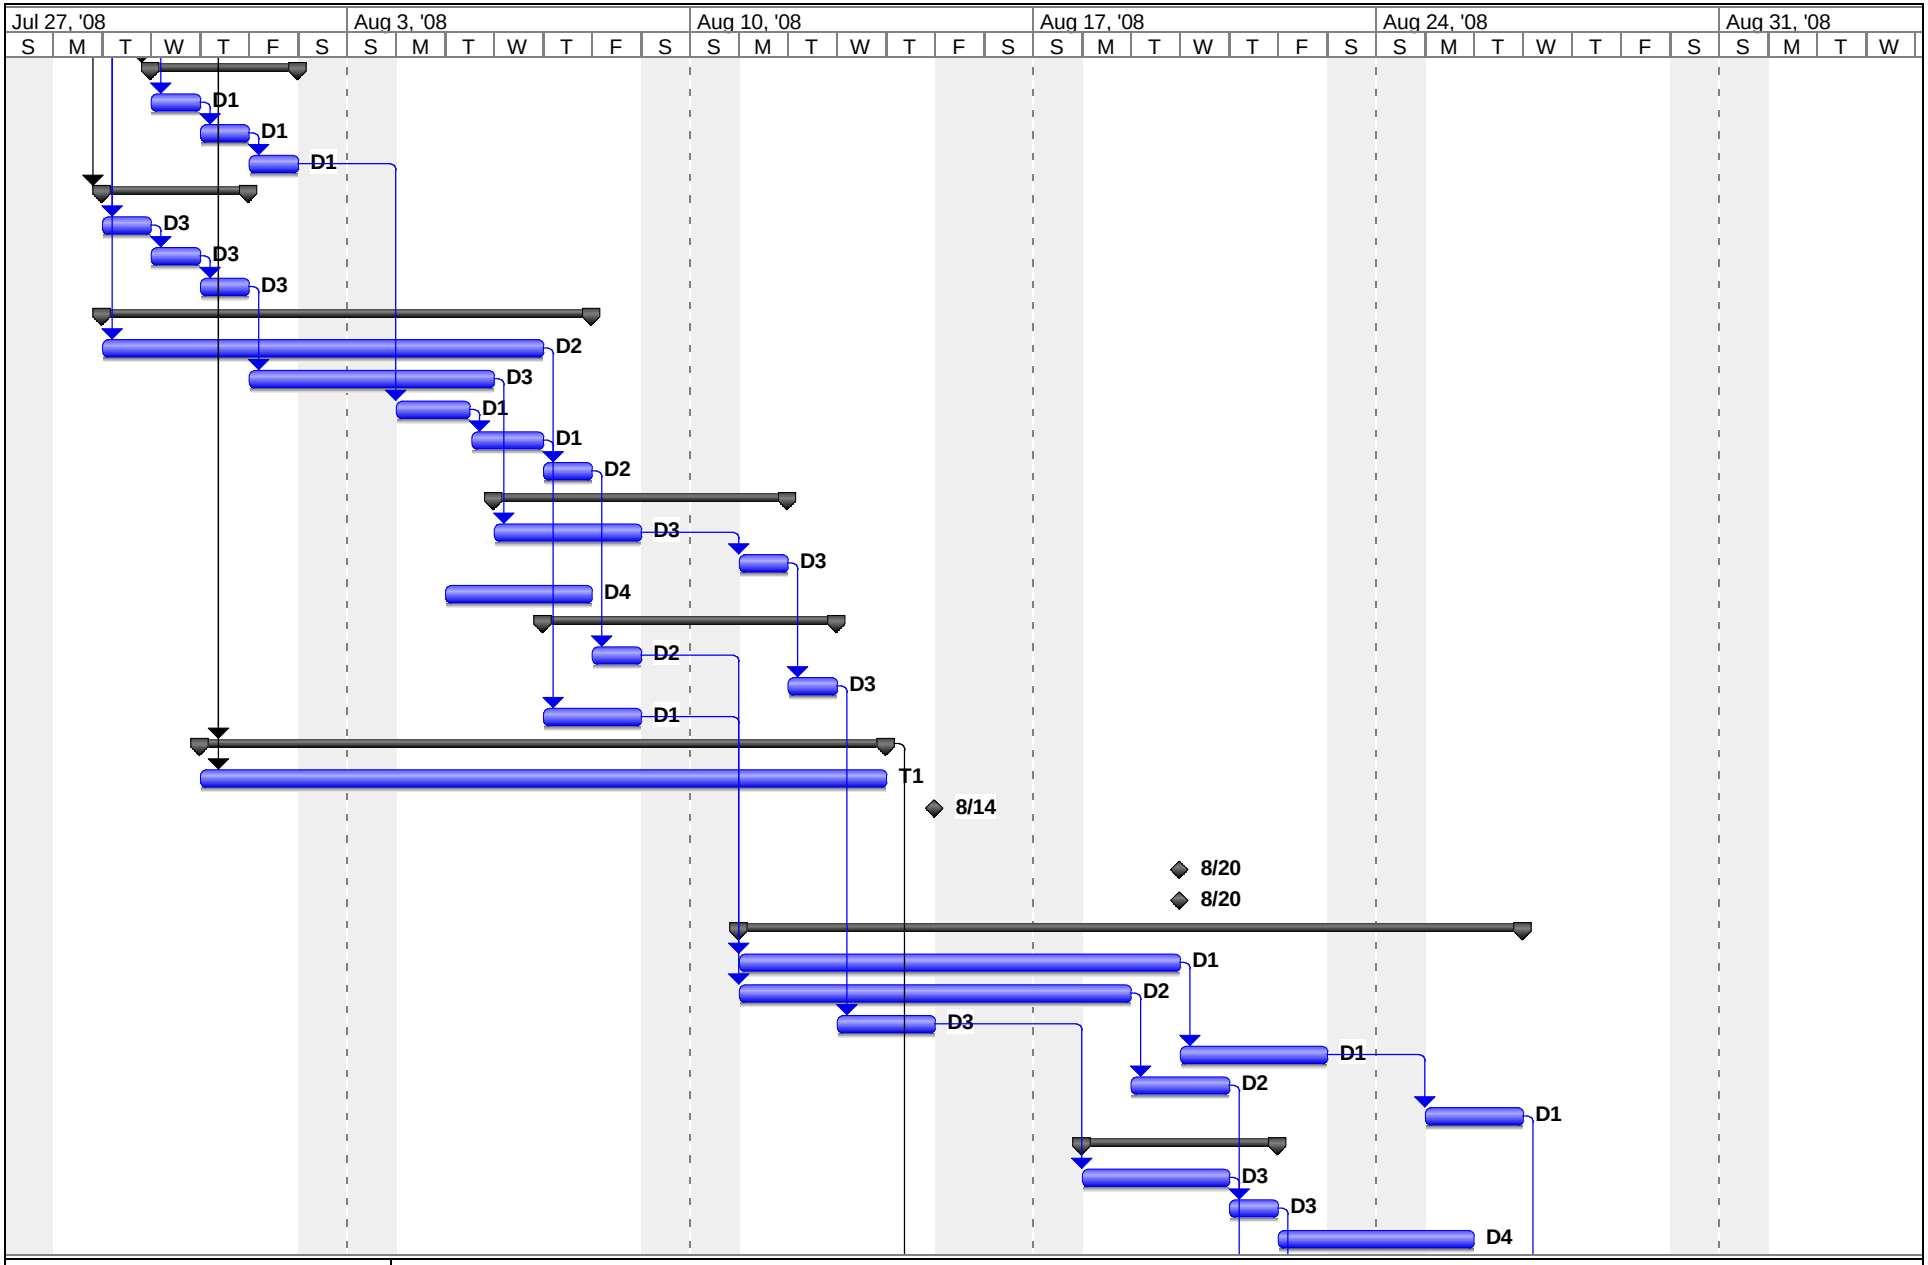

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

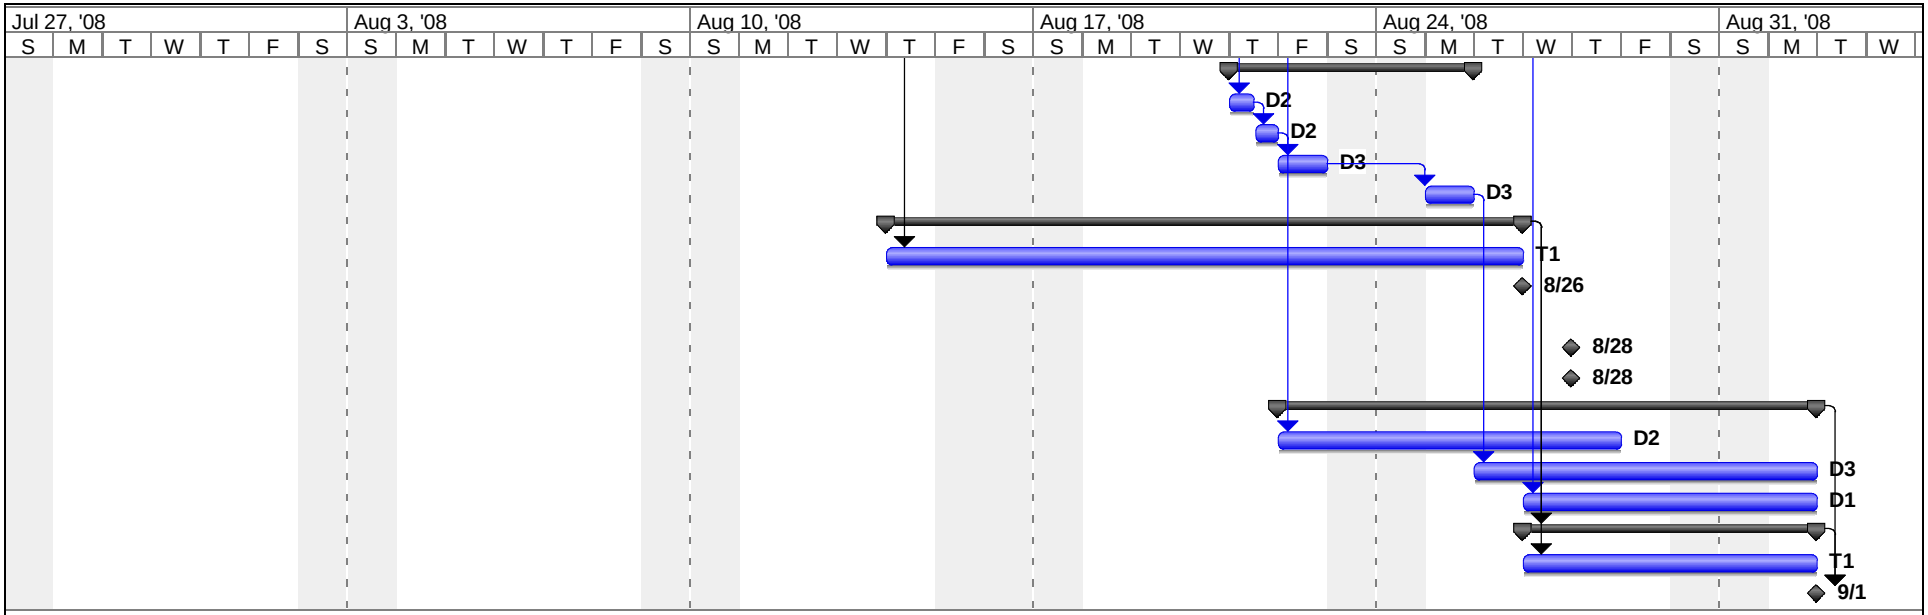

Project: Mezeo for BlackBerry - Project
Date: Wed 6/25/08

Task	Milestone	External Tasks	
Split	Summary	External Milestone	
Progress	Project Summary	Deadline	
